


# Advanta Estimating Sheet

Standard \_\_\_\_\_

Americana \_\_\_\_\_

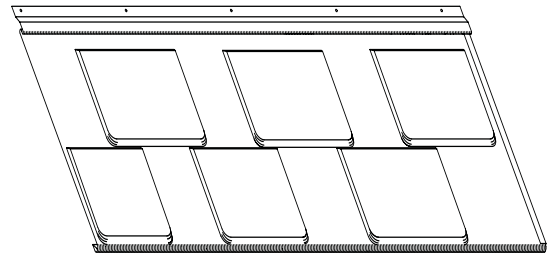

## Panels

Roof Areas :

\_\_\_\_\_ x \_\_\_\_\_ = \_\_\_\_\_ sqft

\_\_\_\_\_ x \_\_\_\_\_ = \_\_\_\_\_ sqft

\_\_\_\_\_ x \_\_\_\_\_ = \_\_\_\_\_ sqft

\_\_\_\_\_ x \_\_\_\_\_ = \_\_\_\_\_ sqft

\_\_\_\_\_ x \_\_\_\_\_ = \_\_\_\_\_ sqft

\_\_\_\_\_ x \_\_\_\_\_ = \_\_\_\_\_ sqft

\_\_\_\_\_ x \_\_\_\_\_ = \_\_\_\_\_ sqft

Total Roof Area = \_\_\_\_\_ sqft

## Trim Components

Eave \_\_\_\_\_

Ridge \_\_\_\_\_

Gable \_\_\_\_\_

Hip \_\_\_\_\_

Headwall \_\_\_\_\_

Sidewall \_\_\_\_\_

Valley \_\_\_\_\_

Shed Ridge \_\_\_\_\_

Enter total footage required for each condition listed above

Panel Square Footage HAS300

Total Roof Area x 1.10 = \_\_\_\_\_ sqft

**Total Cartons** Panel Square Footage div. by 50

\_\_\_\_\_ cartons ( round to nearest full carton )

### Eave

HSA114 Drip edge Eave div. by 9.5 = \_\_\_\_\_ pcs @ 10'-0"

### Gable

HSA114 Drip Edge Gable div. by 9.5 = \_\_\_\_\_ pcs @ 10'-0"

HSA201 Channel Trim Same qty as cap = \_\_\_\_\_ pcs @ 10'-0"

### Ridge

HSA303 Rolled Ridge/Hip cap Ridge div. by 9.5 = \_\_\_\_\_ pcs @ 10'-0"

### Hip

HSA303 Rolled Ridge/Hip cap Ridge div. by 9.5 = \_\_\_\_\_ pcs @ 10'-0"

## Headwall

HSA500 Headwall Headwall div. by 9.5 = \_\_\_\_\_ pcs @ 10'-0"

## Sidewall

HSA411 Sidewall Sidewall div. by 9.5 = \_\_\_\_\_ pcs @ 10'-0"

HSA440 Step Flashing Sidewall x 1 = \_\_\_\_\_ pcs @ 14"

## Valley

HSA801 Valley Valley div. by 9.5 = \_\_\_\_\_ pcs @10'-0"

HSA805 Valley Cover Same qty as Valley = \_\_\_\_\_ pcs @ 10'-0"

## Shed Ridge

HSA342 Shed Ridge Shed Ridge div. by 9.5 = \_\_\_\_\_ pcs @10'-0"

## Accessories

---

HVC903 Valley Clips HSA801 Valley x 12 = \_\_\_\_\_ pcs ( round to nearest 50 )

---

\*\* RSS213 1 1/2" Wafer Head Screws Total Cartons x 150 = \_\_\_\_\_ pcs (round to nearest 100)

OR

\*\* SWR402 2" Ring Shank Grommetted Nails Total Cartons x 150 = \_\_\_\_\_ pcs (round to nearest 100)

---

RSR3xx Rivets Total Roof Area div. by 15 = \_\_\_\_\_ pcs (round to nearest 50)

SWR9XX 2" Ptd Gasketed Screw (HSA303 Rolled Ridge/Hip x 12) + (HSA500 Headwall x 6) +  
(HSA342 Shed Ridge x 12) = \_\_\_\_\_ pcs (round to nearest 100)

SWR8XX 7/8" Ptd Gasketed Stitch Screw HSA805 Valley Cover x 6 = \_\_\_\_\_ pcs (round to nearest 50)

RSC312 Butyl Tape 50' HSA201 Channel Trim + HSA805 Valley Cover div. by 4.5 = \_\_\_\_\_ rolls

RSC350 Expandable Sealant Tape ((HSA303 Rolled Ridge/Hip x 2) + HSA500 Headwall +  
HSA342 Shed Ridge ) div. total by 1.75 = \_\_\_\_\_ pcs

SCR800 Closure Tape HSA303 Rolled Ridge/Hip div. by 4.5 = \_\_\_\_\_ rolls

RST2XX Touch up Paint 2 oz. \_\_\_\_\_ ea
